



Metro

Los Angeles County
Metropolitan Transportation
Authority
One Gateway Plaza
3rd Floor Board Room
Los Angeles, CA

Board Report

File #: 2020-0830, **File Type:** Oral Report / Presentation

Agenda Number: 31.

CONSTRUCTION COMMITTEE JANUARY 21, 2021

SUBJECT: PROGRAM MANAGEMENT MAJOR PROJECT STATUS REPORT

ACTION: ORAL REPORT

RECOMMENDATION

RECEIVE oral report on the Major Project Status by the Chief Program Management Officer.

DISCUSSION


Update report covering the month of January 2021 by the Chief Program Management Officer.

ATTACHMENTS

Attachment A - Program Management Major Project Status Report

Prepared by:

- **Crenshaw/LAX** - Sameh Ghaly, Sr EO Project Mgmt., (213) 418-3369
- **Regional Connector** - Gary Baker, EO Project Mgmt., (213) 893-7191
- **Westside Purple Line Ext 1** - James Cohen, EO Project Mgmt., (213) 922-7911
- **Westside Purple Line Ext 2** - Michael McKenna, EO Project Mgmt., (213) 312-3132
- **Westside Purple Line Ext 3** - Kimberly Ong, EO Project Mgmt., (323) 903-4112
- **Patsaouras Plaza Busway Station** - Timothy Lindholm, EO Project Engr., (213) 922-7297
- **Willowbrook/Rosa Park Station** - Timothy Lindholm, EO Project Engr., (213) 922-7297
- **I-210 Barrier Replacement** - Andrroush Danielians, EO Project Engr., (213) 922-7598
- **I-5 North** - Abdollah Ansari, Sr EO Construction & Engr., (213) 922-4781
- **I-5 South** - Abdollah Ansari, Sr EO Construction & Engr., (213) 922-4781
- **Presentation** - Yohana Jonathan, Mgr, Project Control, (213) 418-3031



Phillip A. Washington
Chief Executive Officer

Program Management Major Project Status Report

Presented By

Richard Clarke


Chief Program Management Officer

Impact of COVID-19 Cases on Construction Projects







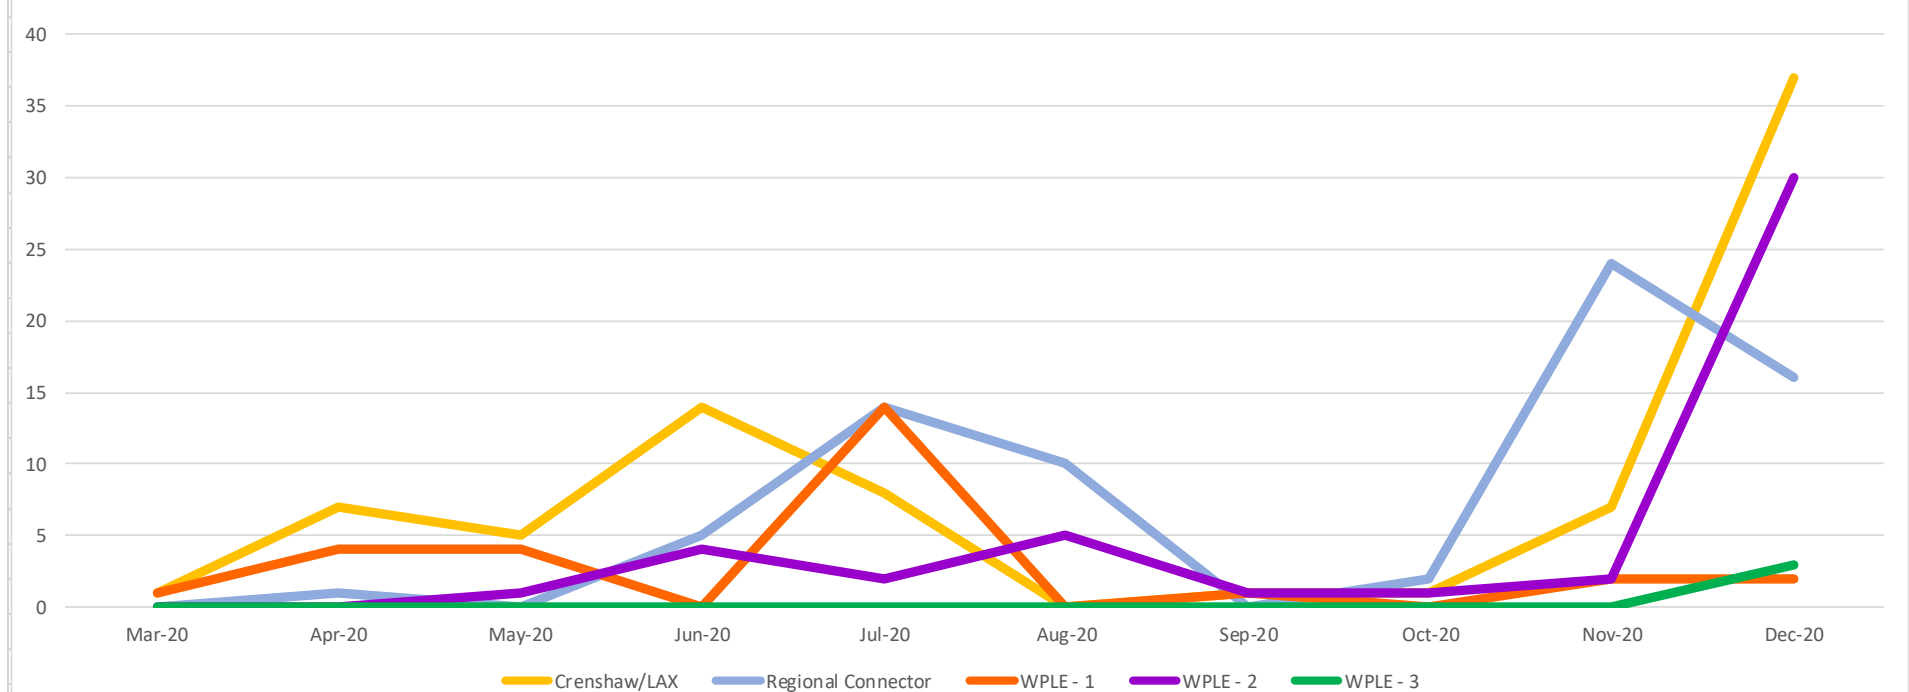













Metro Projects COVID-19 Confirmed Cases

Project	Mar-20	Apr-20	May-20	Jun-20	Jul-20	Aug-20	Sep-20	Oct-20	Nov-20	Dec-20	Total Cases to Date
Crenshaw/LAX	1	7	5	14	8	0	1	1	7	37	81
Regional Connector	0	1	0	5	14	10	0	2	24	16	72
WPLE - 1	1	4	4	0	14	0	1	0	2	2	28
WPLE - 2	0	0	1	4	2	5	1	1	2	30	46
WPLE - 3	0	0	0	0	0	0	0	0	0	3	3

Confirmed COVID-19 Cases



PROJECT BUDGET & SCHEDULE STATUS SUMMARY CHART

Project	Cost Performance	Schedule Performance	Comments
Crenshaw/LAX			Project is 97% complete. Contractor is not applying sufficient work force to complete their remaining work. Metro continues to work with contractor to mitigate the schedule forecast; emphasizing safety and reliability in final acceptance of project elements and systems.
Regional Connector			Project is 72.5% complete. Schedule is being challenged by overbuild requirements at Historic Broadway Station; mitigation plans are being pursued. Largely dependent on schedule, budget options are under review to maximize returns to ensure certainty to post construction rail activation and start-up objectives.
Westside Purple Line Extension-Section 1			Project is 66% complete. Reviewing any impacts differing site conditions and third-party requirements may have on the project schedule. The Reach 3 anomaly is impacting critical path tunnel mining activities.
Westside Purple Line Extension-Section 2			Project is 39% complete and proceeding on schedule and within budget.
Westside Purple Line Extension-Section 3			Project is 16% complete and proceeding on schedule and within budget.
Willowbrook/Rosa Parks Station			Project is 80% complete. The Customer Center, Mobility Hub + Public Plaza and promenade are complete and turned over to Metro in October. Package B grading and underground utility work ongoing. Elevator and stair work at the C Line West entrance is ongoing and expected to open in December.
I-210 Barrier Replacement			Caltrans (CT) Design has approved the Project 1 PS&E package. All CT design comments have been addressed and accepted. However, the encroachment permit for Project 1 can't be granted until the ADL testing has been completed and submitted to Caltrans. Funding source for ADL testing still to be determined. Project 2 Barrier analysis is expected to begin in mid December 2020.
1-5 North County Enhancements			Project is in bidding phase and is expected to begin construction in Spring 2021.
I-5 North: SR 118 to SR 134			Segment 1 and 2 are completed. Segment 3 (Empire Ave & Burbank) is 86% complete. Segment 4 (Magnolia to SR-134) is 97% complete and began the plant establishment phase on June 1, 2020.
I-5 South: Orange County Line to I-605			Segments 1, 3, and the Carmenita Interchange are completed. Segment 2 (Valley View) is 72% complete. Segment 4 (Imperial) is 97% complete and began the plant establishment phase on Jan 31, 2020. Segment 5 (Florence) is 92% complete.

January 2021

Construction Committee

Los Angeles County Metropolitan Transportation Authority



On target



Possible problem



Significant Impact



Metro 3

CRENSHAW/LAX TRANSIT PROJECT

◆ BUDGET

	<u>Current</u>	<u>Forecast</u>
TOTAL COST	\$2,148M	\$2,148M

⚠ SCHEDULE

	<u>Current</u>	<u>Forecast</u>
REVENUE OPERATION	May 2021	TBD - 2021

- Overall Project Progress is 97% complete.
- Contractor is not applying sufficient work force to complete their remaining work.
- Metro continues to work with contractor to mitigate the schedule forecast; emphasizing safety and reliability in final acceptance of project elements and systems.
- Remaining work is primarily systems—power, train control, station/tunnel fire life safety & communications.



P3010 LRT Vehicle testing on Crenshaw Blvd. and 54th Street.



Leimert Park Station – contractor working on communication rack in train control and communication room.

January 2021



On target



Possible problem



Significant Impact



Metro 4

Construction Committee

Los Angeles County Metropolitan Transportation Authority

REGIONAL CONNECTOR TRANSIT PROJECT


BUDGET

	<u>Current</u>	<u>Forecast</u>
TOTAL COST	\$1,816M	\$1,816M

SCHEDULE

	<u>Current</u> Summer/Fall 2022	<u>Forecast</u> Summer/Fall 2022
REVENUE OPERATION		

- Overall Project Progress is 72.5% complete.
- Little Tokyo/Arts District Station & Surrounding Area:** Gold Line Little Tokyo/Arts District Station closed, Central St restoration complete, bus bridge ongoing.
- Historic Broadway and Grand Av Arts/Bunker Hill Station:** Structural concrete, MEP and systems installation continues throughout the Station.
- Flower Street:** Installation of walls, roof and MEP near completion for tie-in to 7th/Metro Station.
- Trackwork:** Installation efforts underway in all reaches; special trackwork procurements experiencing fabrication delays.

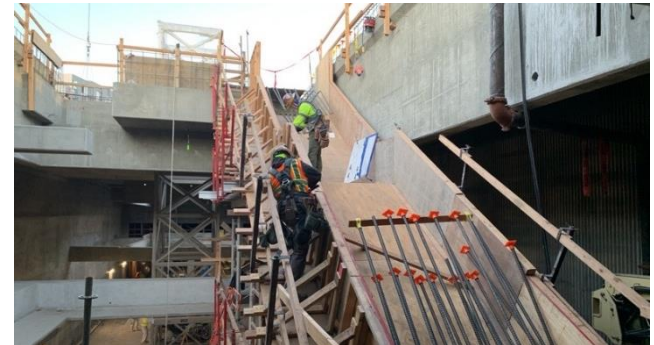

Forming for stairs in future Little Tokyo /Arts District Station



Backfill operations over station box at Historic Broadway Station

January 2021



On target



Possible problem



Significant Impact



Metro 5

Construction Committee

Los Angeles County Metropolitan Transportation Authority

WESTSIDE PURPLE LINE EXTENSION – SECTION 1

BUDGET

	<u>Current</u>	<u>Forecast</u>
TOTAL COST*	\$3,354M	\$3,354M


* Includes Board approved LOP budget plus finance costs.

SCHEDULE

	<u>Current</u>	<u>Forecast</u>
REVENUE	Fall	Fall
OPERATIONS	2024 (FFGA)	2023

Overall Project Progress is 66% complete.

- Wilshire/Western Retrieval Shaft:** Continued support of Reach 1 cross passage work. Minor work on break through into Wilshire/Western Station continues on weekends.
- Wilshire/La Brea Station:** With the exception of the West Hammerhead, all roof concrete placements (Blocks 1-13) have been completed. Backfill (above the roof) activities, plenum work and appendage construction continue.
- Wilshire/Fairfax Station:** Concourse and 2nd lift wall concrete activities are scheduled for December 2020 and January 2021. Entrance plaza and appendage work continue.
- Wilshire/La Cienega Station:** Roof concrete placements continue through the month of December 2020. Concrete placement of the protection slab at the entrance structure is also scheduled in the month of December 2020.
- Tunneling:** The Purple TBM (Elsie) has mined 2,828 feet (86% complete) and is parked 75' from the anomaly site. The Red TBM (Soyeon) has mined 2,734 feet (83% complete) and is parked 190' from the anomaly site. Mining will continue once the Wilshire/San Vicente grout block installation is completed.
- Reach 1 Tunnel Cross Passages (CP):** 9 out of 12 cross passages have been excavated. Concrete placement for 4 cross passages have been completed (#10, #11, #13, #15). Work continues at all other cross passages. Completion is planned for February 2021.
- Schedule:** The Reach 3 anomaly is significantly impacting critical path tunnel mining activities. The project is attempting to mitigate the delay. The forecast completion is currently the second half of 2024. Metro and the FTA will have a formal risk assessment after mining through the anomaly is completed in April 2021. The Board will be briefed on the results of the risk assessment.

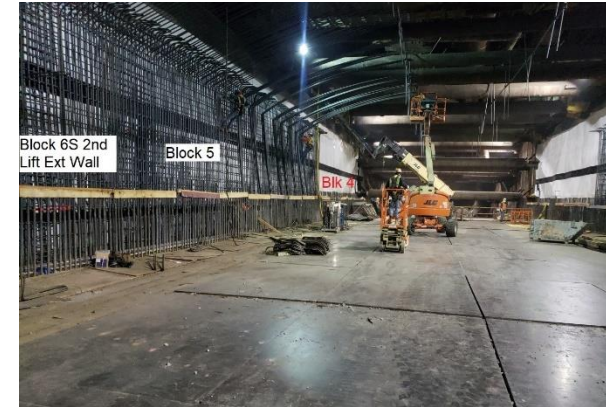

Wilshire/Fairfax Station 2nd Lift Wall Rebar installation



Track Level Conduit Installation at Wilshire/La Brea

January 2021

Construction Committee

Los Angeles County Metropolitan Transportation Authority



On target



Possible problem



Significant Impact

WESTSIDE PURPLE LINE EXTENSION – SECTION 2



BUDGET

	<u>Current</u>	<u>Forecast</u>
TOTAL COST*	\$2,530M	\$2,530M

* Includes Board approved LOP budget plus finance costs.



SCHEDULE

	<u>Current</u>	<u>Forecast</u>
REVENUE	Winter	Summer
OPERATION	2026 (FFGA)	2025

- Overall Project progress is 39% complete.

Century City Constellation Station

- Pile installation on Constellation Boulevard west of the TBM launch box is anticipated to be completed in January 2021 and the decking operations are anticipated to be completed in April 2021.

Wilshire/Rodeo Station

- Excavation of the station box and entrance is continuing with an anticipated completion in February 2021.
- On November 10, 2020, the Beverly Hills City Council approved the settlement agreement to end the city's lawsuit against the FTA and Metro.

Tunneling

- The abandonment of both oil wells on the Beverly Hills High School campus is complete.
- BL TBM "Ruth" was re-launched on November 23, 2020 after successful completion of the remaining oil well abandonment work. BR activity will resume once BL TBM breaks out of tunnel access shaft east wall.
- Once both TBMs pass through the tunnel access shaft, tunneling operations will be transitioned to the access shaft from the existing TBM launch box area.



Piling and Decking Installation West of the TBM Launch Box



Excavation of the Wilshire/Rodeo Station



On target



Possible problem



Major issue

January 2021

Construction Committee

Los Angeles County Metropolitan Transportation Authority



Metro 7

WESTSIDE PURPLE LINE EXTENSION – SECTION 3



BUDGET

	<u>Current</u>	<u>Forecast</u>
TOTAL COST*	\$3,611M	\$3,611M


* Includes Board approved LOP budget plus finance costs.



SCHEDULE

	<u>Current</u>	<u>Forecast</u>
REVENUE	Winter	Spring
OERATION	2028 (FFGA)	2027

- Overall Project progress is 16% complete
- Final design progress is 73% complete
- **C1151 Tunnel Contract**
 - TBM #1 continues mining the BR tunnel.
 - TBM #2 assembly continues at the BL headwall.
 - Fabrication of tunnel precast concrete liners are ongoing.
 - Installation of instrumentation and monitoring equipment are ongoing.
- **C1152 Stations, Trackwork, and Systems Contract**
 - Final design is ongoing.
 - Westwood/VA Station SCE power conduit installation along Wilshire Boulevard is on-going; completion expected in December 2020.
 - Site clearing in VA Parking Lot 42 commenced November 2020.
- **Other Work**
 - Cable pulling/splicing in the joint trench (Verizon and Frontier) at the Westwood/UCLA Station expected in December 2020. LADWP power cutover to the 10921 Wilshire Boulevard building is scheduled by spring of 2021.
 - VA shuttle and valet service started in November 2020.

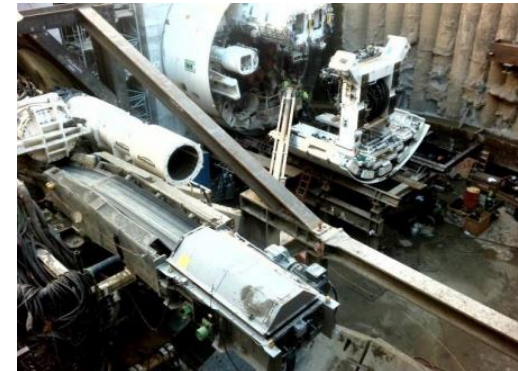

TBM Assembly at Tail Track Exit Shaft



Installation of SCE Ductbank & Substructure at Bonsall Entrance Ramp

January 2021



On target



Possible problem



Significant Impact



Metro 8

Construction Committee

Los Angeles County Metropolitan Transportation Authority

WILLOWBROOK/ROSA PARKS STATION

BUDGET

	<u>Current</u>	<u>Forecast</u>
TOTAL COST	\$128.4M	\$128.4M

SCHEDULE

	<u>Current</u>	<u>Forecast</u>
SUBSTANTIAL COMPLETION	March 2021	March 2021

- Package A: Customer Center, Mobility Hub and Public Plaza substantially complete and turned over to Metro for Soft Public Opening in October. Final repairs to the Landscaping within the Public Plaza are ongoing with completion expected by the end of December.
- Package C: Remaining punch list and finish work ongoing throughout the platform.
- Package B: Package B underground utility work ongoing with hardscape work proceeding at the central plaza. Trench work and soil removal in progress for new Gross Solid Removal Device (GSRD). Work at elevator 4 at the C Line West Entrance is ongoing with temporary sidewalk and state inspection approval expected by end of December.



Mobility Hub, Customer Service Building and Public Plaza complete for soft opening



Utility Work @ Package B



Hardscape Work @ Central Plaza

January 2021



On target



Possible problem



Significant Impact



Metro 9

Construction Committee

Los Angeles County Metropolitan Transportation Authority

I-210 BARRIER REPLACEMENT PROJECT


BUDGET

	<u>Current</u>	<u>Forecast</u>
TOTAL COST	\$22.54M	\$22.54M
	Design	Design

SCHEDULE

	<u>Current</u>	<u>Forecast</u>
Complete Design (Proj 1)	Dec 2020	Fall 2020
Complete Design (Proj 2)	Aug 2022	Summer 2022

- Project 1: Segment from Michillinda to Iconic Bridge – Caltrans (CT) Design has approved the Project 1 PS&E package. All CT Design comments have been addressed and accepted. However, the encroachment permit for Project 1 can't be granted until the ADL testing has been completed. Funding source for ADL testing still to be determined.
- Project 2: Segment from west end of the project to Michillinda – Barrier analysis is expected to begin in mid-December 2020.

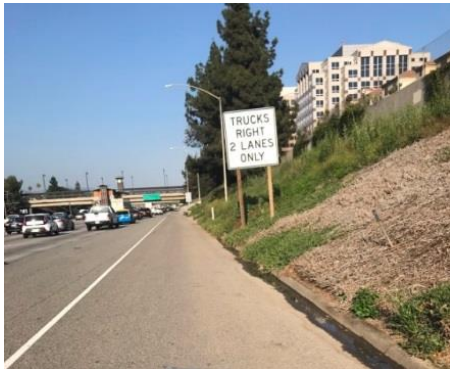

Newly Installed Caltrans Freeway Sign



Incident in 2014



Newly Installed Speed Limit Sign

January 2021



On target



Possible problem



Significant Impact



Metro 10

Construction Committee

Los Angeles County Metropolitan Transportation Authority

I-5 Construction Projects (Administered by Metro)



January 2021

Construction Committee

Los Angeles County Metropolitan Transportation Authority

I-5 NORTH COUNTY ENHANCEMENTS



BUDGET

	<u>Current</u>	<u>Forecast</u>
TOTAL COST	\$679.3M	\$679.3M



SCHEDULE

	<u>Current</u>	<u>Forecast</u>
SUBSTANTIAL COMPLETION	March 2026	March 2026

- Project is in procurement phase and is expected to begin construction in Spring 2021.



Old Road-SCE Power & AT&T Relocation



Gavin Canyon Over-crossing-SCE Power & AT&T Relocation



Biscailuz Over-crossing AT&T Horizontal Directional Drill under I-5



January 2021



On target



Possible problem



Significant Impact



Metro 12

Construction Committee

Los Angeles County Metropolitan Transportation Authority

I-5 Construction Projects (By Caltrans)



I-5 NORTH: SR 118 TO SR 134




⚠ BUDGET

	Current	Forecast
TOTAL COST	\$880.9M	\$954.1M*

⚠ SCHEDULE

ANTICIPATED PROJECT COMPLETION	Current Summer 2022	Forecast* Winter 2022
--------------------------------	------------------------	--------------------------

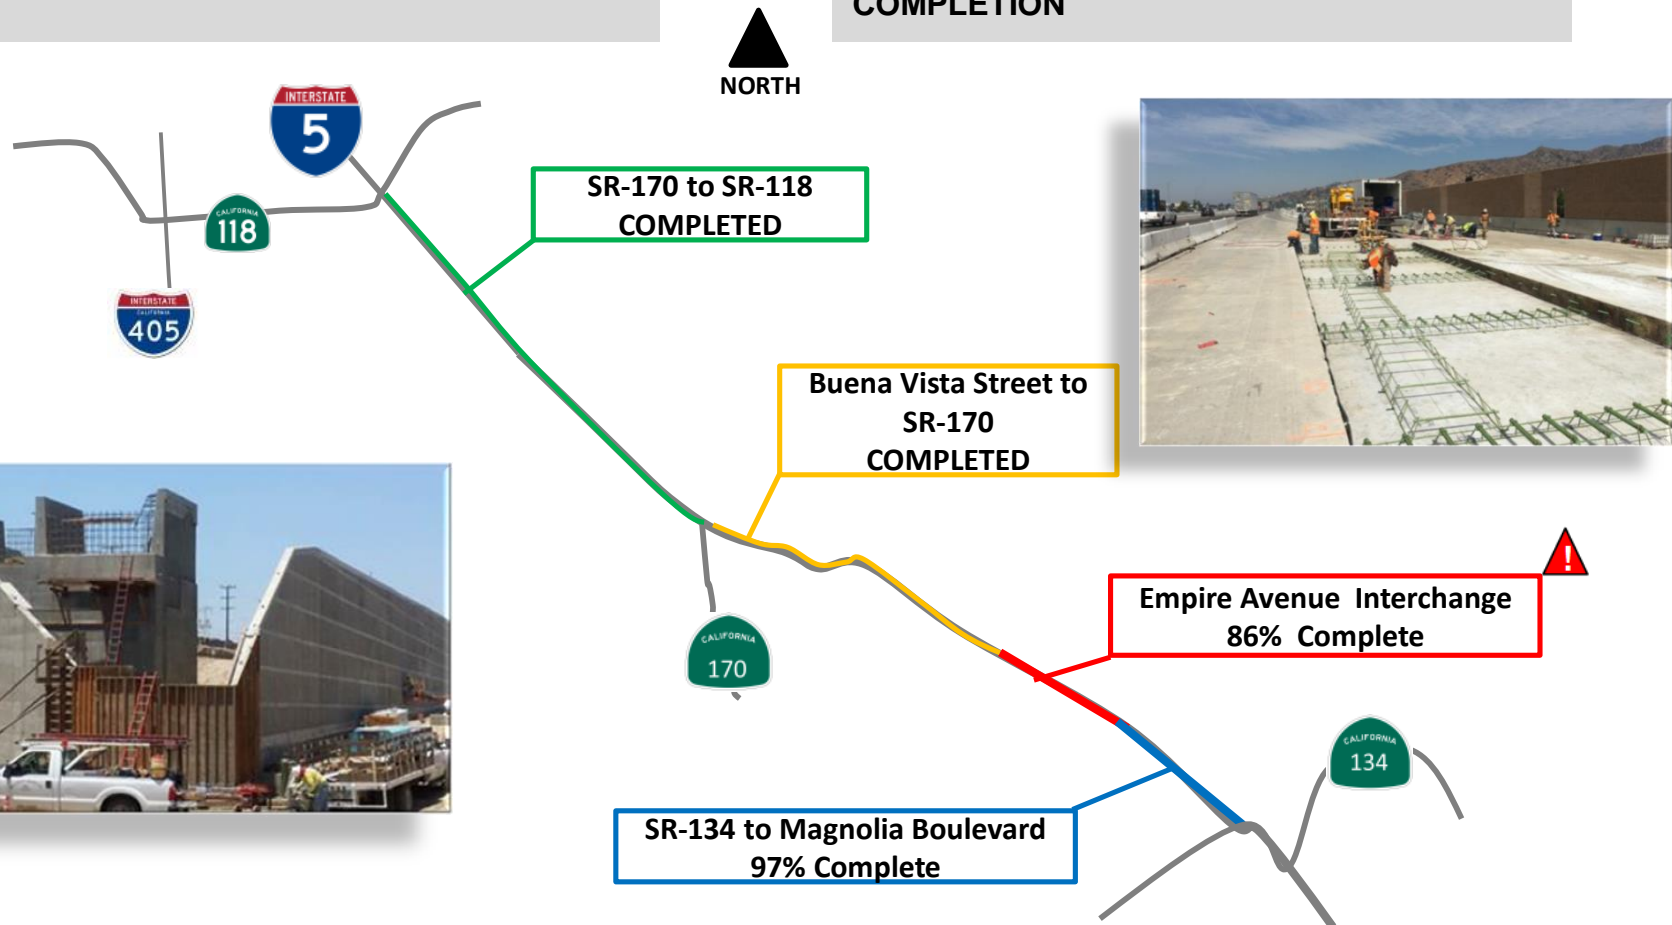

January 2021

Construction Committee

Los Angeles County Metropolitan Transportation Authority

I-5 SOUTH: ORANGE COUNTY LINE TO I-605



BUDGET

	Current	Forecast
TOTAL COST	\$1.888B	\$1.888B*




SCHEDULE

**ANTICIPATED
PROJECT
COMPLETION**

Current
Fall 2022

Forecast*
Winter 2022

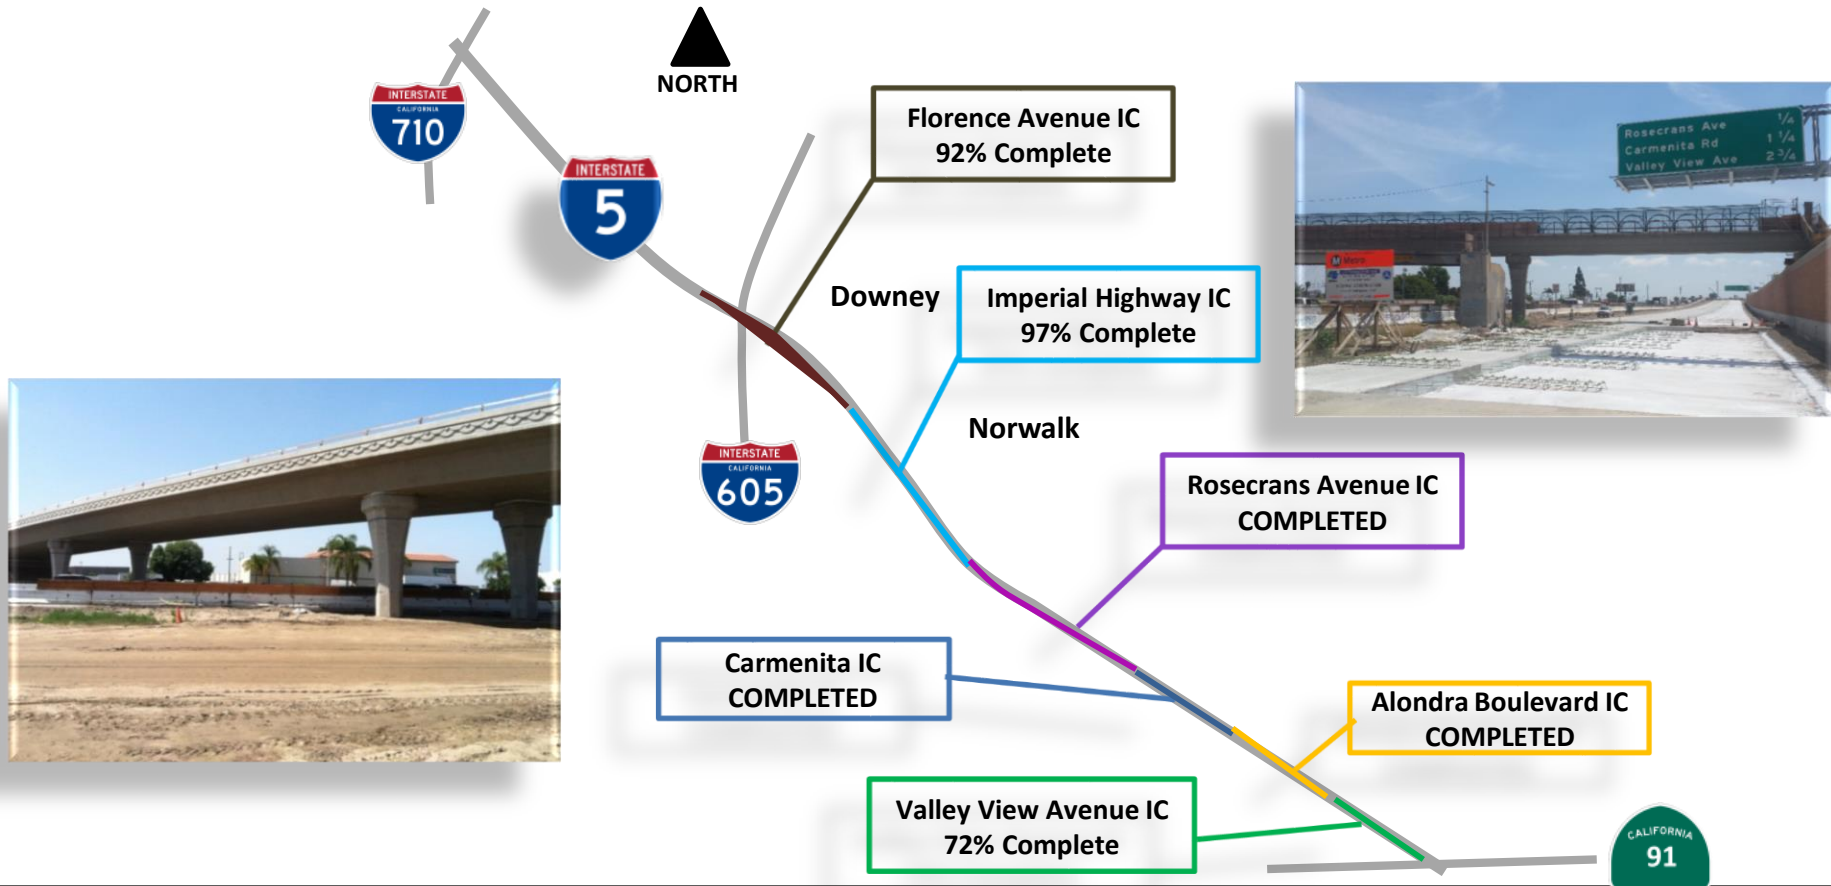

January 2021

Construction Committee

Los Angeles County Metropolitan Transportation Authority



On target



Possible problem



Significant Impact



Metro 15

* Risk Analysis, Nov 2020
