



Metro

Los Angeles County
Metropolitan Transportation
Authority
One Gateway Plaza
3rd Floor Board Room
Los Angeles, CA

Board Report

File #: 2020-0890, File Type: Oral Report / Presentation

Agenda Number: 30.

CONSTRUCTION COMMITTEE FEBRUARY 18, 2021

SUBJECT: PROGRAM MANAGEMENT MAJOR PROJECT STATUS REPORT

ACTION: ORAL REPORT

RECOMMENDATION

RECEIVE oral report on the Major Project Status by the Chief Program Management Officer.

DISCUSSION

Update report covering the month of February 2021 by the Chief Program Management Officer.

Prepared by:

- **Crenshaw/LAX** - Sameh Ghaly, Sr EO Project Mgmt., (213) 418-3369
- **Regional Connector** - Gary Baker, EO Project Mgmt., (213) 893-7191
- **Westside Purple Line Ext 1** - James Cohen, EO Project Mgmt., (213) 922-7911
- **Westside Purple Line Ext 2** - Michael McKenna, EO Project Mgmt., (213) 312-3132
- **Westside Purple Line Ext 3** - Kimberly Ong, EO Project Mgmt., (323) 903-4112
- **Patsaouras Plaza Busway Station** - Timothy Lindholm, Sr. EO Project Engr., (213) 922-7297
- **Willowbrook/Rosa Park Station** - Timothy Lindholm, Sr. EO Project Engr., (213) 922-7297
- **I-210 Barrier Replacement** - Androush Danielians, EO Project Engr., (213) 922-7598
- **I-5 North** - Abdollah Ansari, Sr EO Construction & Engr., (213) 922-4781
- **I-5 South** - Abdollah Ansari, Sr EO Construction & Engr., (213) 922-4781
- **Presentation** - Shannon Hanley, Mgr, Project Control, (213) 922-1350



Phillip A. Washington
Chief Executive Officer

Program Management Major Project Status Report

Presented By

Richard Clarke


Chief Program Management Officer

Impact of COVID-19 Cases on Mega Construction Projects (as of 1/31/2021)

Metro Mega Construction Projects COVID-19 Confirmed Cases





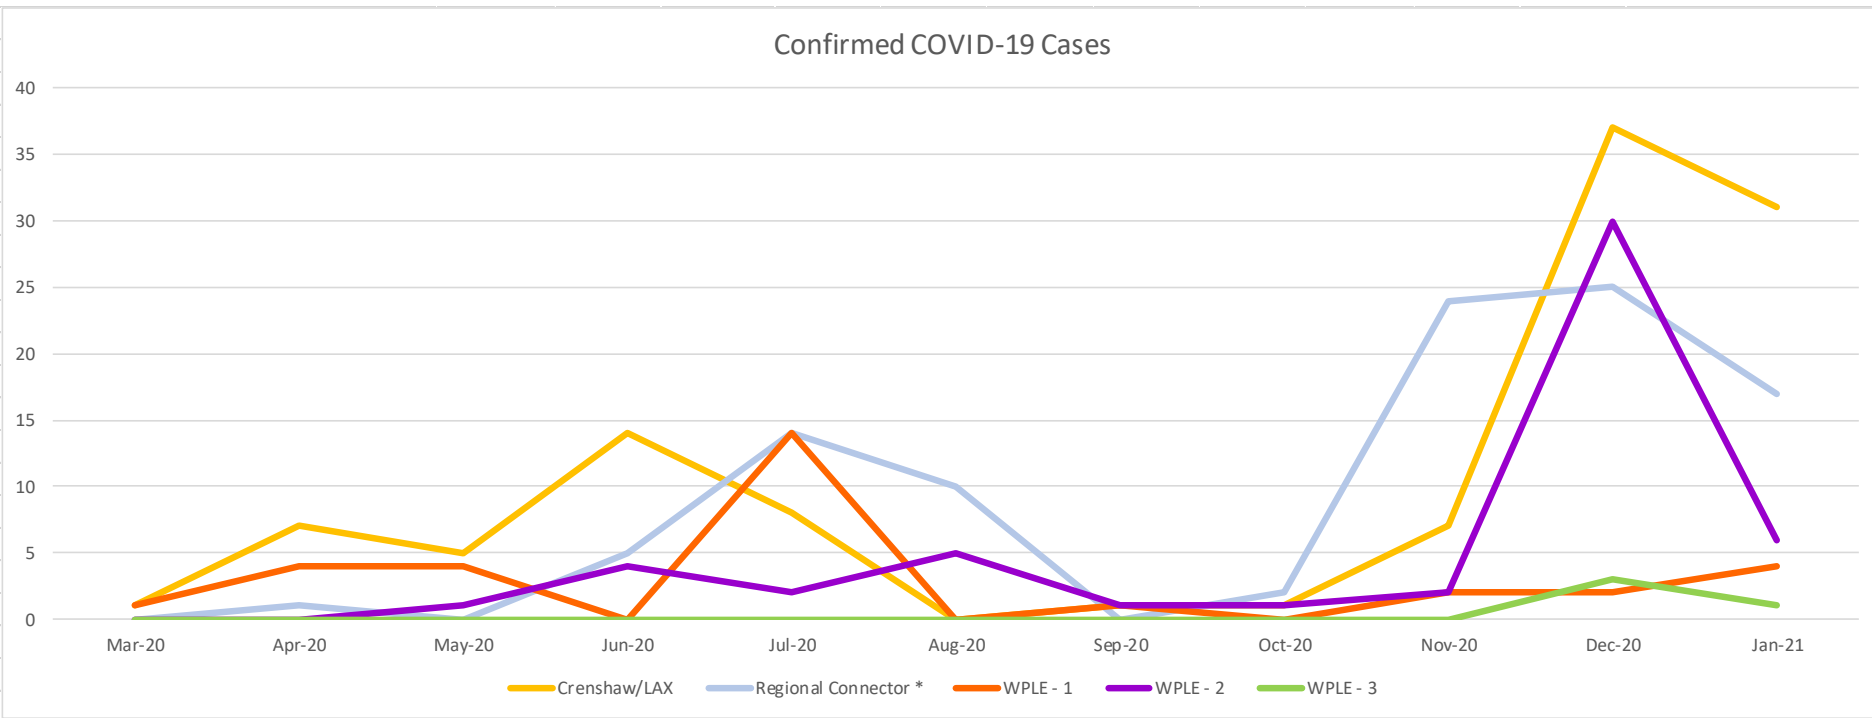















Project	Mar-20	Apr-20	May-20	Jun-20	Jul-20	Aug-20	Sep-20	Oct-20	Nov-20	Dec-20	Jan-21	Total Cases to Date
Crenshaw/LAX	1	7	5	14	8	0	1	1	7	37	31	112
Regional Connector *	0	1	0	5	14	10	0	2	24	25	17	98
WPLE - 1	1	4	4	0	14	0	1	0	2	2	4	32
WPLE - 2	0	0	1	4	2	5	1	1	2	30	6	52
WPLE - 3	0	0	0	0	0	0	0	0	0	3	1	4

Confirmed COVID-19 Cases



*Regional Connector case count for December 2020 was revised due to a January 2021 audit

PROJECT BUDGET & SCHEDULE STATUS SUMMARY CHART

Project	Cost Performance	Schedule Performance	Comments
Crenshaw/LAX			Project is 98% complete. Contractor is not applying sufficient work force to complete their remaining work. Metro continues to work with contractor to mitigate the schedule forecast; emphasizing safety and reliability in final acceptance of project elements and systems.
Regional Connector			Project is 74% complete. Schedule agreement seemed to mitigate Load Transfer System (LTS) delays and accelerate balance of Project; civil and structural giving way to systems and finishes in all areas except Alameda and 1st St; backfill and restorations at stations continue to gain pace.
Westside Purple Line Extension-Section 1			Project is 67% complete. Reviewing the impacts differing site conditions and third-party requirements have had on the project schedule. The Reach 3 anomaly is impacting critical path tunnel mining activities.
Westside Purple Line Extension-Section 2			Project is 41% complete and proceeding on schedule and within budget.
Westside Purple Line Extension-Section 3			Project is 18% complete and proceeding on schedule and within budget.
Willowbrook/Rosa Parks Station			The Customer Center, Mobility Hub + Public Plaza and promenade are complete and turned over to Metro. Package B is in full progress with underground utility work and vertical circulation work. Elevator #4 at the C Line West entrance, a major phase for the project, is expected to be completed by 1 st quarter 2021.
I-210 Barrier Replacement			Caltrans (CT) Design has approved Project 1's Plans, Specifications and Estimate (PS&E) package. However, the construction permit for Project 1 will be granted once the Aerially Deposited Lead (ADL) testing has been completed and submitted to Caltrans. Funding source for ADL testing still to be determined. Project 2 Barrier analysis has begun in late January. Development of Project Study Report (PSR) for Project 2 is underway.
1-5 North County Enhancements			Project is in procurement and is expected to begin construction in Summer 2021.
I-5 North: SR 118 to SR 134			Segment 1 and 2 are completed. Segment 3 (Empire Ave & Burbank) is 87% complete. Segment 4 (Magnolia to SR-134) is 98% complete and began the plant establishment phase on June 1, 2020.
I-5 South: Orange County Line to I-605			Segments 1, 3, and the Carmenita Interchange are completed. Segment 2 (Valley View) is 74% complete. Segment 4 (Imperial) is 97% complete and began the plant establishment phase on Jan 31, 2020. Segment 5 (Florence) is 92% complete.

February 2021

Construction Committee

Los Angeles County Metropolitan Transportation Authority



On target



Possible problem



Significant Impact



Metro 3

CRENSHAW/LAX TRANSIT PROJECT

◆ BUDGET

	<u>Current</u>	<u>Forecast</u>
TOTAL COST	\$2,148M	\$2,148M

⚠ SCHEDULE

	<u>Current</u>	<u>Forecast</u>
REVENUE OPERATION	May 2021	TBD - 2021

- Overall Project Progress is 98% complete.
- Contractor is not applying sufficient work force to complete their remaining work.
- Metro continues to work with contractor to mitigate the schedule forecast; emphasizing safety and reliability in final acceptance of project elements and systems.
- Remaining work is primarily systems—power, train control, station/tunnel fire life safety & communications.



LEIMERT PARK STATION – Continue performing electrical work to the Fare Gate/TVM system at the Paid & Free Area.



UNDERGROUND STRUCTURE NO. 3 – Start-up crew inspecting fans

February 2021



On target



Possible problem



Significant Impact



Metro 4

Construction Committee

Los Angeles County Metropolitan Transportation Authority

REGIONAL CONNECTOR TRANSIT PROJECT

BUDGET

	<u>Current</u>	<u>Forecast</u>
TOTAL COST	\$1,816M	\$1,816M

SCHEDULE

	<u>Current</u> Summer/Fall 2022	<u>Forecast</u> Summer/Fall 2022
REVENUE OPERATION		

- Overall Project Progress is 74% complete.
- Little Tokyo/Arts District Station & Surrounding Area:** Utility work and excavation for underground guideway beneath Temple Street is advancing.
- Historic Broadway Station:** Construction work on the entrance structure including the overbuild structure foundation work is continuing.
- Grand Av Arts/Bunker Hill Station:** Approaching final concrete pours; Pedestrian Bridge construction over Hope underway.
- Flower Street:** Concrete nearing completion; final walkways and Mechanical, Electrical, & Plumbing (MEP) underway; interface plans with 7th/Metro Station under review.
- Trackwork:** Crossover installation east of Broadway Station underway; Trackwork between 7th/Metro and Little Tokyo/Arts District Station complete.
- Systems:** Overhead Conductor Rail (OCR) layout initiated with access from Alameda Wye to 7th/Metro Station.



Conduit installation inside CMU Walls at
Grand Av Art/Bunker Hill Station



Backfill operations above roof slab at Flower St

February 2021



On target



Possible problem



Significant Impact



Metro 5

Construction Committee

Los Angeles County Metropolitan Transportation Authority

WESTSIDE PURPLE LINE EXTENSION – SECTION 1

◆ BUDGET

	<u>Current</u>	<u>Forecast</u>
TOTAL COST*	\$3,354M	\$3,354M

* Includes Board approved LOP budget plus finance costs.

⚠ SCHEDULE

	<u>Current</u>	<u>Forecast</u>
REVENUE	Fall	Fall
OPERATIONS	2024 (FFGA)	2023

Overall Project Progress is 67% complete.

Wilshire/La Brea Station: Permanent utility installation / backfill (above the roof) activities, plenum work and appendage construction continue.

Wilshire/Fairfax Station: Concourse and 2nd lift wall concrete activities continue. Entrance plaza and appendage work move forward. Build out of roof forming systems is scheduled to start in January 2021.

Wilshire/La Cienega Station: Roof concrete placements continue through the month of February 2021. Work on the entrance structure also moves forward. Preparation for Tunnel Boring Machine (TBM) arrival continues.


Tunneling: The Purple TBM (Elsie) has mined 2,828 feet (86% complete) and is parked 75' from the anomaly site. The Red TBM (Soyeon) has mined 2,734 feet (83% complete) and is parked 190' from the anomaly site. Mining will continue once the Wilshire/San Vicente grout block installation is completed.

Reach 1 Tunnel Cross Passages (CP): 11 out of 12 cross passages have been excavated. Concrete placement for 5 cross passages are complete (#10, #11, #13, #14, #15). Completion of all Reach 1 cross passages is planned for February 2021.

Schedule: The Reach 3 anomaly is significantly impacting critical path tunnel mining activities. The project is attempting to mitigate the delay. The forecast completion is currently the 4th quarter of 2024. Metro and the FTA will have a formal risk assessment after mining through the anomaly is completed in April 2021. The Board will be briefed of the results of the risk assessment.



Wilshire/La Brea Concrete Placement Above Station Roof

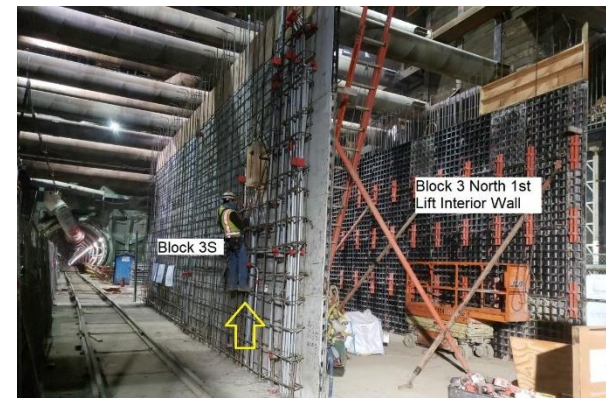

Interior Wall Conduit Installation at Wilshire/Fairfax

February 2021

Construction Committee

Los Angeles County Metropolitan Transportation Authority



On target



Possible problem



Significant Impact

WESTSIDE PURPLE LINE EXTENSION – SECTION 2



BUDGET

	<u>Current</u>	<u>Forecast</u>
TOTAL COST*	\$2,530M	\$2,530M

* Includes Board approved LOP budget plus finance costs.




SCHEDULE

	<u>Current</u>	<u>Forecast</u>
REVENUE	Winter	Summer
OPERATION	2026 (FFGA)	2025

- Overall Project progress is 41% complete.
- **Century City Constellation Station**
 - On January 5, 2021, the City of Los Angeles approved additional street closures along Constellation Boulevard between Avenue of the Stars and Solar Way through April 4, 2021, including 13 weekend closures at the intersection of Constellation Boulevard and Avenue of the Stars.
 - Pile installation on Constellation Boulevard is anticipated to be completed in February 2021.
 - Decking operations are anticipated to be completed in April 2021.
- **Wilshire/Rodeo Station**
 - Excavation of the station is anticipated to be completed in February 2021.
- **Tunneling**
 - Tunneling operations are progressing. The BL TBM “Ruth” is east of the buildings on the Beverly Hills High School campus. The BR TBM “Harriet” is scheduled to be east of the high school buildings in late February 2021.
 - After the BR TBM reaches the tennis courts on the high school campus, all tunneling operations will be transitioned from the TBM Launch Box area to the access shaft.



Tunnel Access Shaft

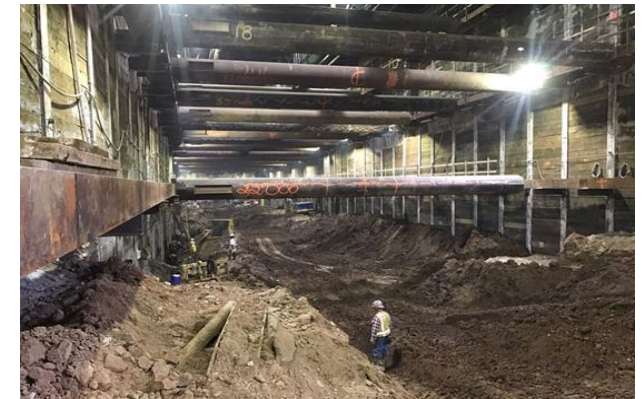

Excavation - Wilshire/Rodeo Station



On target



Possible problem



Major issue



Metro 7

February 2021

Construction Committee

Los Angeles County Metropolitan Transportation Authority

WESTSIDE PURPLE LINE EXTENSION – SECTION 3



BUDGET

	<u>Current</u>	<u>Forecast</u>
TOTAL COST*	\$3,611M	\$3,611M

* Includes Board approved LOP budget plus finance costs.



SCHEDULE

	<u>Current</u>	<u>Forecast</u>
REVENUE	Winter	Spring
OERATION	2028 (FFGA)	2027

- Overall Project progress is 18% complete
- Final design progress is 77% complete
- **C1151 Tunnel Contract**
 - TBM #1 (BR) has mined the initial 112 feet and is being fitted with gantries 2, 3, & 4 before resuming mining.
 - TBM #2 (BL) assembly continues at the BL headwall.
 - Fabrication of tunnel precast concrete liners are ongoing.
 - Installation of instrumentation and monitoring equipment is ongoing.
 - Special segment mold build and Aerially Deposited Lead removal proceeding.
- **C1152 Stations, Trackwork, and Systems Contract**
 - Final design is ongoing.
 - Westwood/VA Station power conduit installation along Wilshire Boulevard complete; ductbank installation on VA Lot 42 completion expected in January 2021.
 - VA solar panel removal completed in VA Lot 42; site preparation and soundwall installation expected to be complete in January 2021.
 - Utility relocation at UCLA and VA Stations sites planned to start in January/February 2021.
- **Other Work**
 - Joint trench for Verizon and Frontier telecommunications is substantially complete; punch list expected to be complete January 2021.
 - LADWP power cutover to 10921 Wilshire Boulevard is planned for spring of 2021.



BL TBM Assembly at Tail Track Exit Shaft



Installation of Sound Wall at the VA Site

February 2021



On target



Possible problem



Significant Impact



Metro 8

Construction Committee

Los Angeles County Metropolitan Transportation Authority

WILLOWBROOK/ROSA PARKS STATION

BUDGET

	<u>Current</u>	<u>Forecast</u>
TOTAL COST	\$128.4M	\$128.4M

SCHEDULE

	<u>Current</u>	<u>Forecast</u>
SUBSTANTIAL COMPLETION	March 2021	March 2021

- Package A: Customer Center, Mobility Hub and Public Plaza substantially complete and turned over to Metro. Final repairs to the Landscaping within the Public Plaza are ongoing.
- Package C: Remaining punch list and finish work ongoing throughout the platform.
- Package B: Package B underground utility work ongoing with underground utility work throughout. Installation of new County required storm drain in progress. Elevator 4 work at the C Line West Entrance is ongoing with temporary sidewalk and state inspection approval expected by end of February. Once certified, the project will be cleared to close up the entire central plaza for main Package B work.



Mobility Hub, Customer Service Building and Public Plaza complete and open to the public



Infrastructure Work @ Central Plaza



Storm Drain Work @ Central Plaza



Phase 1 Street Work completed

February 2021



On target



Possible problem



Significant Impact



Metro 9

Construction Committee

Los Angeles County Metropolitan Transportation Authority

I-210 BARRIER REPLACEMENT PROJECT


BUDGET

	<u>Current</u>	<u>Forecast</u>
TOTAL COST	\$22.54M	\$22.54M
	Design	Design

SCHEDULE

	<u>Current</u>	<u>Forecast</u>
Complete Design (Proj 1)	Feb 2021	Winter 2021
Complete Design (Proj 2)	Aug 2022	Summer 2022

- Project 1: Segment from Michillinda to Iconic Bridge – Caltrans (CT) Design has approved Project 1's Plans, Specifications and Estimate (PS&E) package. However, the construction permit for Project 1 will be granted once the Aerially Deposited Lead (ADL) testing has been completed. Funding source for ADL testing still to be determined.
- Project 2: Segment from west end of the project to Michillinda – Barrier analysis has begun in late January. Development of Project Study Report (PSR) for Project 2 is underway.

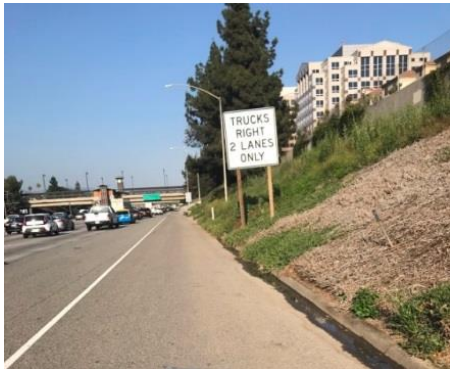

Newly Installed Caltrans Freeway Sign





Incident in 2014




Newly Installed Speed Limit Sign

February 2021

 On target


 Possible problem

 Significant Impact

Construction Committee

Los Angeles County Metropolitan Transportation Authority

I-5 Construction Projects (Administered by Metro)

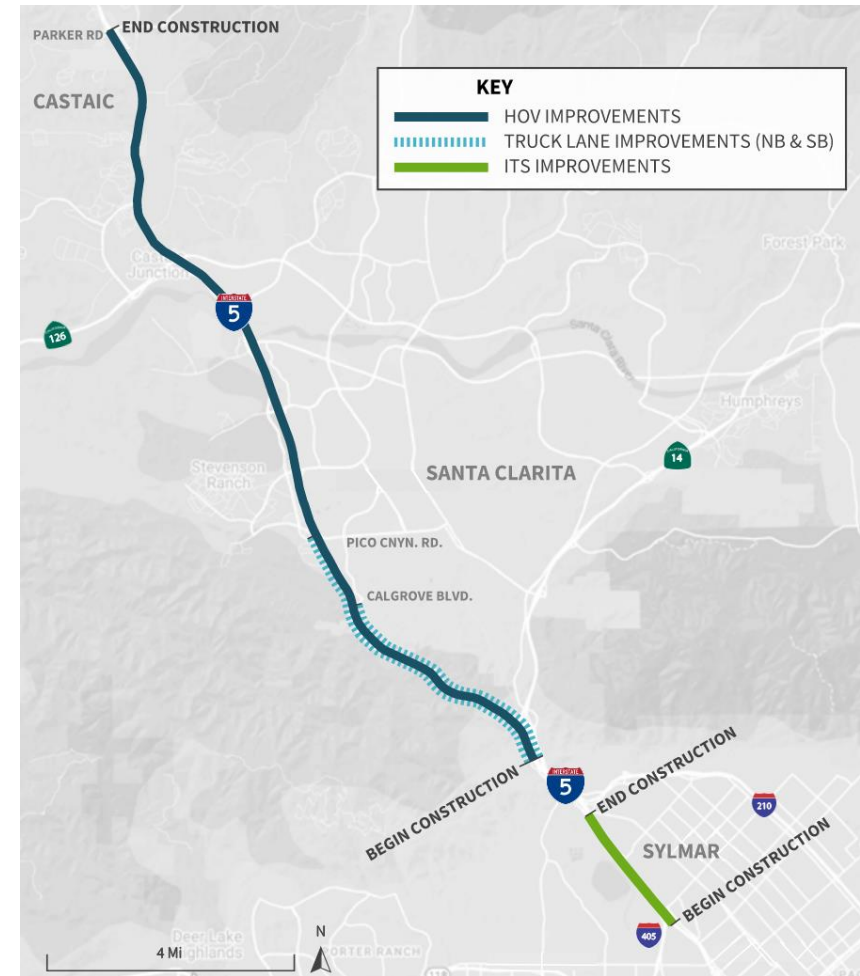

February 2021

Construction Committee

Los Angeles County Metropolitan Transportation Authority

I-5 NORTH COUNTY ENHANCEMENTS



BUDGET

	<u>Current</u>	<u>Forecast</u>
TOTAL COST	\$679.3M	\$679.3M



SCHEDULE

	<u>Current</u>	<u>Forecast</u>
SUBSTANTIAL COMPLETION	Spring 2026	Spring 2026

- Project is in procurement phase and is expected to begin construction in Summer 2021.
- Advanced utility relocations on-going



Old Road-SCE Power & AT&T Relocation



Gavin Canyon Over-crossing-SCE Power & AT&T Relocation



Biscailuz Over-crossing AT&T Horizontal Directional Drill under I-5



February 2021



On target



Possible problem



Significant Impact



Metro 12

Construction Committee

Los Angeles County Metropolitan Transportation Authority

I-5 Construction Projects (By Caltrans)



I-5 NORTH: SR 118 TO SR 134




⚠ BUDGET

	Current	Forecast
TOTAL COST	\$880.9M	\$954.1M*

⚠ SCHEDULE

ANTICIPATED PROJECT COMPLETION	Current Summer 2022	Forecast* Winter 2022
--------------------------------	------------------------	--------------------------

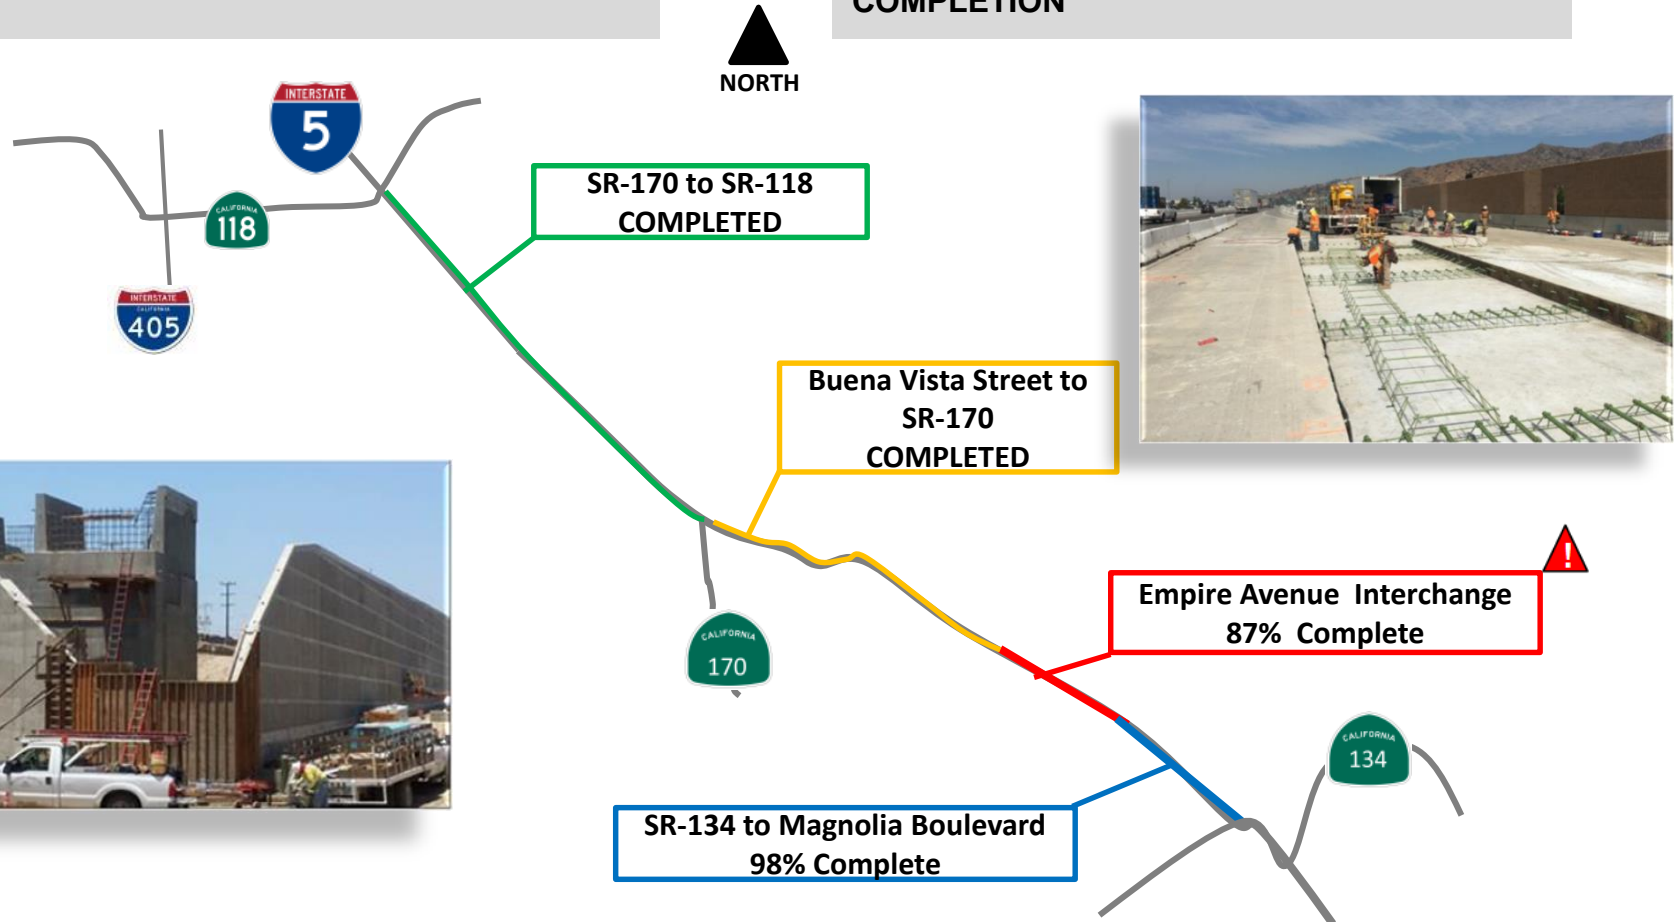

February 2021

Construction Committee

Los Angeles County Metropolitan Transportation Authority

I-5 SOUTH: ORANGE COUNTY LINE TO I-605



BUDGET

	Current	Forecast
TOTAL COST	\$1.888B	\$1.888B*




SCHEDULE

**ANTICIPATED
PROJECT
COMPLETION**

Current
Winter 2022

Forecast*
Spring 2023

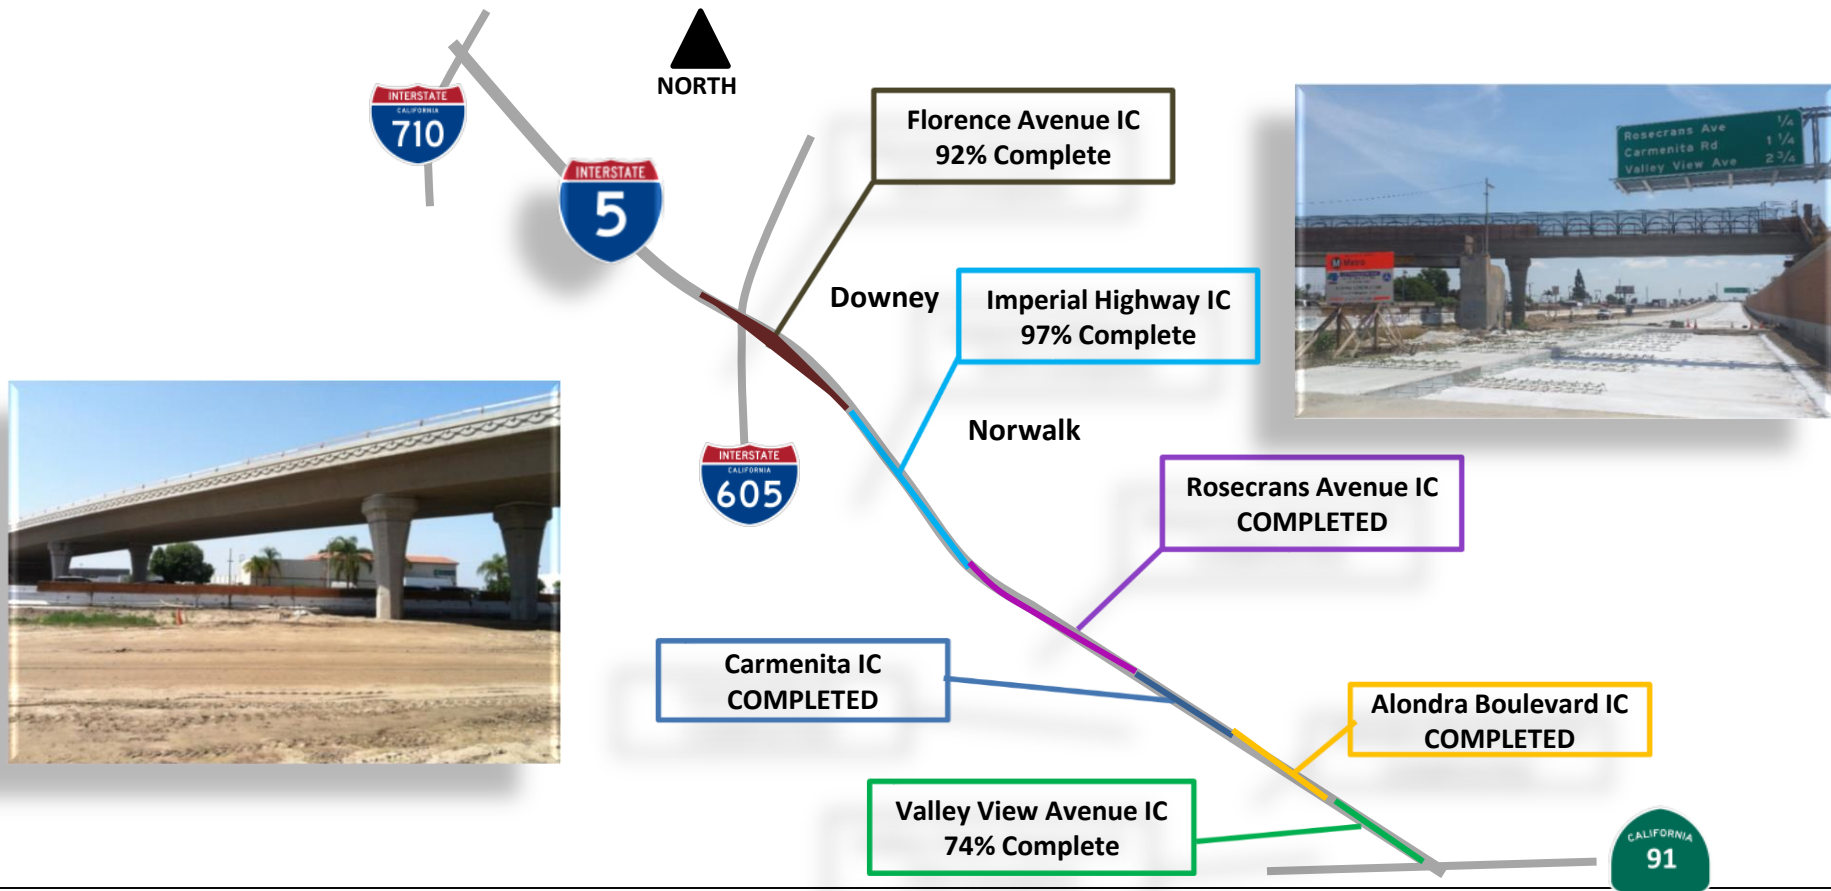

February 2021

Construction Committee

Los Angeles County Metropolitan Transportation Authority



On target



Possible problem



Significant Impact



Metro 15

* Risk Analysis, Nov 2020
