

**Board Report**

File #: 2021-0025, **File Type:** Informational Report**Agenda Number:** 14.

**PLANNING AND PROGRAMMING COMMITTEE
MARCH 17, 2021****SUBJECT: COUNTYWIDE PLANNING MAJOR PROJECT STATUS REPORT****ACTION: RECEIVE AND FILE****RECOMMENDATION**

RECEIVE AND FILE monthly report on the Major Capital Projects in the environmental planning phase by the Chief Planning Officer.

DISCUSSION

- **East San Fernando Valley LRT**

The Metro Board certified the EIR on December 3, 2020 and the FTA issued the Record of Decision on January 29, 2021. With the CEQA document certified and the Record of Decision issued by the FTA for the NEPA document, the Project is environmentally cleared. With this significant Project milestone completed, Program Management has initiated the process of right-of-way acquisitions, potholing, and utility relocations for the Initial Project Segment on Van Nuys Boulevard between the Metro Orange Line and San Fernando Road. The Project's draft 30%/60% design drawings are currently being circulated for comment and review with Metro departments.

On December 3, 2020, the Board directed that further study be conducted for the 2.5-mile segment of the project in the Metro-owned Antelope Valley Railroad Right-of-Way. Staff, in coordination with the City of San Fernando, City of Los Angeles and the Southern California Regional Rail Authority, is finalizing a scope of work and schedule for this section of the alignment with special attention to railroad grade crossings. An overview of that work was presented to the Planning & Programming Committee at its February 2021 meeting.

- **West Santa Ana Branch Corridor**

The West Santa Ana Branch (WSAB) project is finalizing the second Administrative Draft EIS/R incorporating the first round of Federal Transit Administration (FTA) comments on the Administrative Draft submitted in late November 2020. The second Administrative Draft is scheduled to be submitted on March 16, 2021. Staff continues to coordinate with various third

parties as necessary including Union Pacific Railroad, cities, Caltrans, U.S. Army Corps of Engineers and various utility providers.

Staff is planning to engage key stakeholders before the release of the Draft Environmental document to outline draft environmental review and comment process. The project continues to advance field survey work and verification of existing utilities identified as part of the 15% design.

- **Green Line to Torrance LRT Extension**

The EIR scoping period is proceeding for a 45-day review period which started on January 29 and extends through March 15 with virtual scoping meetings held on February 23 (Agency), 24 and 27, 2021.

The scoping meetings were well attended with over 200 participants on Wednesday, February 24, and over 100 participants on Saturday, February 27. The comments received during the scoping meetings included direction on environmental topics to be studied during the DEIR phase, concerns regarding the alternatives under evaluation, and design features that should be included for consideration (i.e. pedestrian/bicycle access, soundwalls, grade separations, and extended aerial/trench configurations). Comments received are being documented and will be considered and evaluated during the project development process of the project.

- **Eastside Corridor LRT Extension**

Meetings with all corridor cities to solicit input on the Draft Advanced Conceptual Engineering in their respective jurisdictions have been completed.

- City of Whittier (November 18)
- City of Pico Rivera (December 15)
- City of Santa Fe Springs (December 21)
- City of Commerce (January 20)
- City of Montebello (February 11)

Subsequent meetings were held per the cities' requests to either provide an overview of the Draft Advanced Conceptual Engineering to elected officials or discuss specific project elements within the city's respective jurisdictions. Formal comments on the Draft Advanced Conceptual Engineering were submitted by all Cities.

- City of Whittier City Council Ad-hoc (January 7).
- City of Pico Rivera - City-led Rio Hondo Bridge Improvement Project (January 19)
- Washington Coalition (February 4)
- City of Pico Rivera - Right-of-Way needs (February 11)
- City of Commerce - Follow-up (March 4)

Ongoing monthly updates to the Washington Coalition will continue to keep corridor cities current

with project milestones and outreach. The next meeting is on April 1, 2021.

A Community Based Organization (CBO) strategy is being developed for the project in collaboration with the Race and Equity and Community Relations Departments. The strategy's objectives are to work with CBOs and stakeholders that understand the corridor communities to help guide the project's outreach approach and identify ways to solicit project input from CBOs. Metro staff is also closely working with the Metro Board staff to optimize the strategy.

Contract modifications for the environmental and engineering consultants were executed in February. Both consultant teams are advancing the project per the Board's decisions to focus on the Washington Alternative and CEQA only. The engineering consultants have been tasked with refining the Draft Advanced Conceptual Engineering based on comments and evaluating cost-saving opportunities along the alignment.

- **Sepulveda Transit Corridor**

Metro's internal review of private sector PDA proposals has been completed and proposed recommendations for contract award were brought to the Board for review in February. The official recommendation for contract award will occur at the March Board meeting.

The PDA procurement blackout period has ended and PDA concepts have been disclosed. Once approved by the Board, the environmental scoping period can proceed. The environmental review process will be presented to the Board in April and will be formally initiated through public scoping meetings in fall 2021.

- **NoHo to Pasadena Bus Rapid Transit (BRT)**

The NoHo to Pasadena BRT Draft EIR comment period began on October 26 and concluded on December 28. Staff received nearly 500 comments with the majority of them indicating general support for the project. Currently the most challenging issues include community concerns over parking loss along Olive Avenue in Burbank and other comments pertaining to the Eagle Rock section of the project.

In Eagle Rock, most comments favor routing the BRT along Colorado Boulevard rather than on the SR-134 freeway. However, the community has expressed concerns over impacts to the existing buffered bike lanes, medians, traffic, and parking. Several comments have expressed support for a new BRT concept on Colorado Boulevard referred to as the "Beautiful Boulevard", which was developed by a local community group. Staff is currently examining this concept and how its key elements compare to the existing alternatives analyzed in the DEIR.

As of February, staff has begun re-engaging with key stakeholders to work through these remaining issues. In Eagle Rock specifically, two stakeholder roundtables are being planned for mid-March to discuss BRT design concepts on Colorado Boulevard in an effort to strike a balance between some of the competing priorities expressed by community members. The primary goal of this additional stakeholder outreach is to help inform the next step in the process, which is to

develop a recommended Proposed Project. Key details contained in the Proposed Project will include a final project alignment, station locations, and a specific BRT configuration along each segment of the alignment (i.e. center-running, side-running, or curb-running bus lanes). Staff is also planning on conducting an additional community meeting to present and discuss the ultimate Proposed Project prior to presenting it to the Metro Board for approval.


Staff currently intends to return to the Metro Board in May 2021 with two recommendations, including 1) selecting the Proposed Project and 2) approving the Project's Title VI Service Equity Analysis. If the Board approves both recommendations, staff will begin work on the Final EIR and advance the selected BRT design.

ATTACHMENTS

Attachment A - Countywide Planning Monthly Major Projects - March 2021

Prepared by: Dolores Roybal-Saltarelli, DEO, Countywide Planning & Development, (213) 922-3024
Cory Zelmer, DEO, Countywide Planning & Development, (213) 922-1079
David Mieger, SEO, Countywide Planning & Development, (213) 922-3040

Reviewed by: James de la Loza, Chief Planning Officer, (213) 922-2920



Phillip A. Washington
Chief Executive Officer

Countywide Planning Monthly Major Projects

March 2021 Monthly Update


> Monthly Status of Major Projects

- East San Fernando Valley LRT
- West Santa Ana Branch
- Green Line to Torrance
- Eastside 2 Extension
- Sepulveda Transit Corridor
- NoHo to Pasadena BRT

> Capital Investment Grant Priorities Assessment Process



ESFV + Pillar Projects Measure M Baseline Schedules

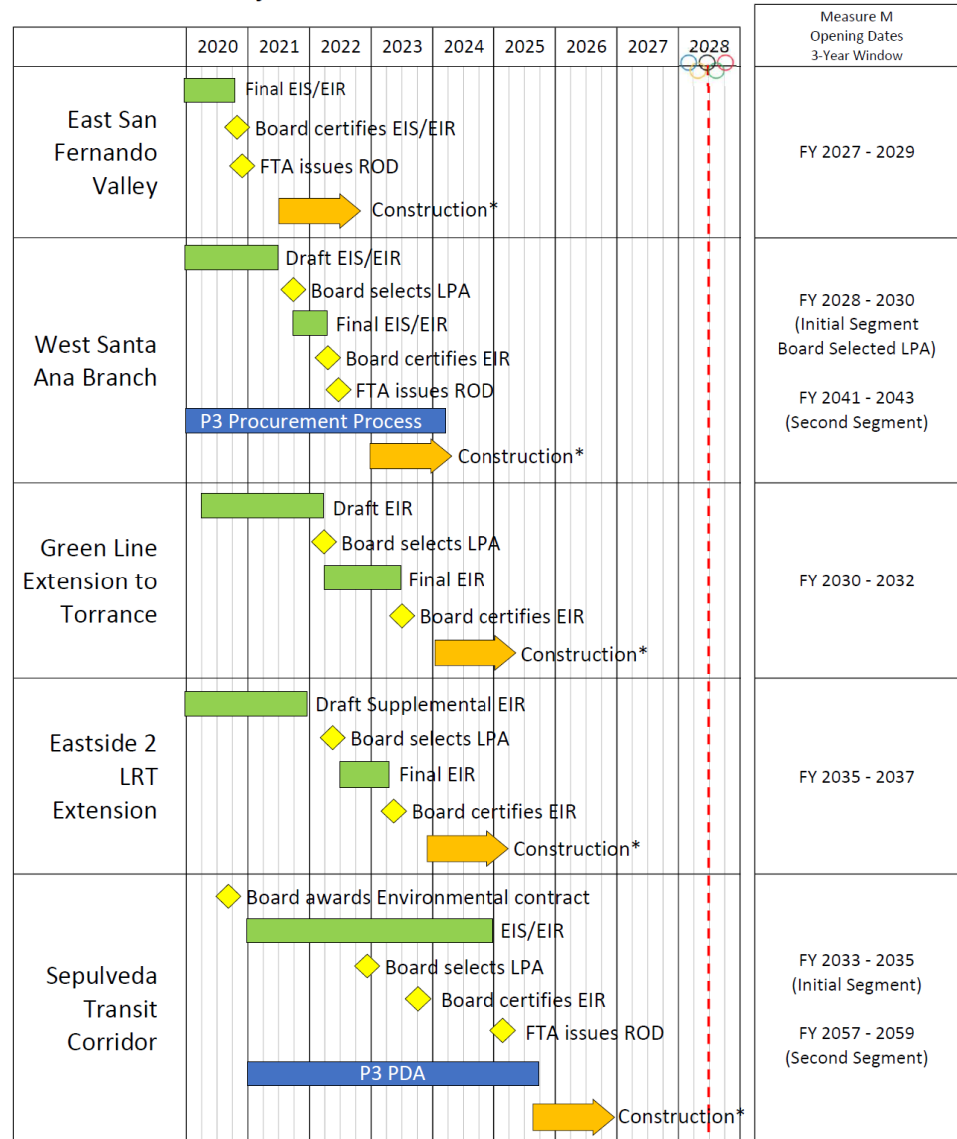

* Construction is inclusive of advanced utility relocation and right-of-way
Schedules are subject to change based on funding and environmental review

East San Fernando Valley LRT



> Status


- Metro Board Certification of CEQA Final EIR on December 3, 2020
- Record of Decision for federal NEPA environmental clearance signed by FTA on January 29, 2021.

> Key Activities

- The San Fernando Road Shared Railroad ROW study work is being initiated in coordination with City of San Fernando communities of Sylmar and Pacoima and SCRRRA. In February 2021, the Scope and Schedule for Supplemental ROW Study was presented to the Planning & Programming Committee.

> Next Actions

- Negotiation of task order for the San Fernando Road Shared Rail Road Right of Way Study.

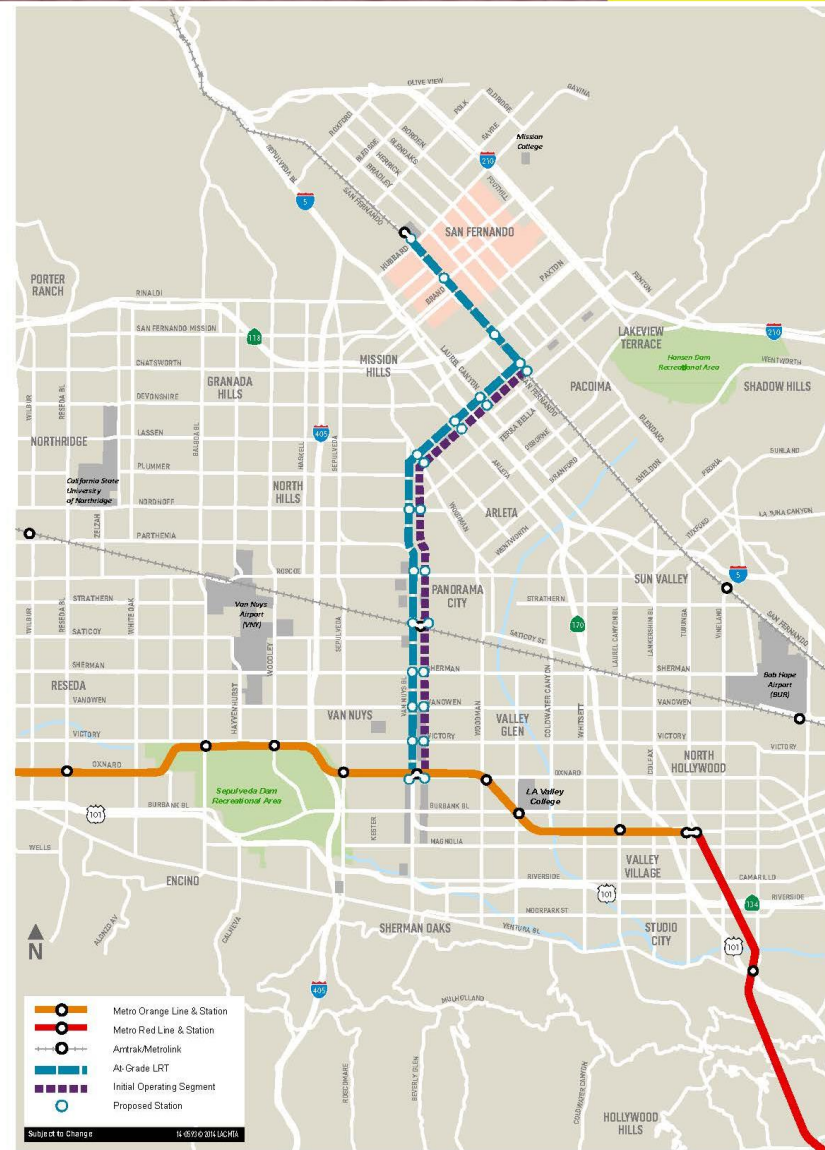

West Santa Ana Branch Transit Corridor



> Status

- Draft EIS/R
 - Second Admin Draft FTA Review: March 19, 2020
 - Anticipated Draft Release: June 2021
 - Anticipated LPA Selection: Sept 2021

> Key Activities

- Working sessions with FTA & Metro Legal to address first round of Admin Draft comments

> Next Actions

- Present updated project cost estimates and funding strategy in April
- Early key stakeholder meetings before release of Draft EIS/EIR to outline review and comment process



Green Line Extension to Torrance

> Status


- Draft EIR + Advanced Conceptual Engineering tasks are proceeding (15% design)

> Key Activities

- Coordination with BNSF on shared track segments
- Engineering analysis of Hawthorne versus ROW technical issues
- Environmental background documentation
- Environmental Scoping Comment Period conducted on January 29 – March 15
- Virtual Scoping Meetings on February 23 (Agency), 24 and 27
- Monthly Board Staff Briefing on March 12

> Next Actions

- Targeted Outreach to Stakeholders
 - City staff
 - South Bay COG
 - Neighborhood associations
 - Other stakeholders
- Recording and documentation of scoping comments is proceeding.

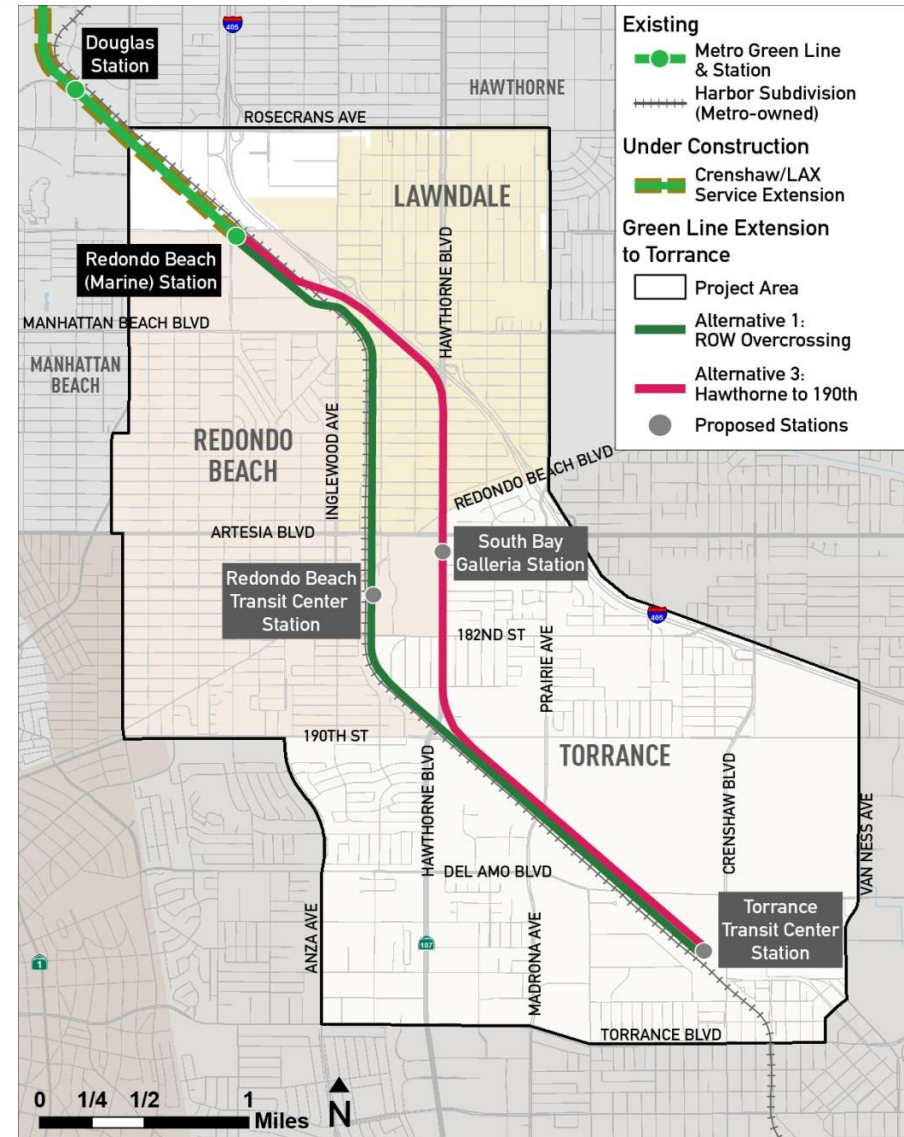


Eastside Transit Corridor Phase 2

> Status

- Systems Engineering and Advanced Conceptual Engineering (ACE) are in progress

> Key Activities

- Contract Modifications were executed for environmental and engineering design
- Project team completed all reviews of the Draft ACE with the following corridor cities:
 - City of Whittier (November 18)
 - City of Pico Rivera (December 15)
 - City of Santa Fe Springs (December 21)
 - City of Commerce (January 20)
 - City of Montebello (February 11)
- Developing a Community Based Organization approach in collaboration with Race and Equity, Community Relations and Board Staff

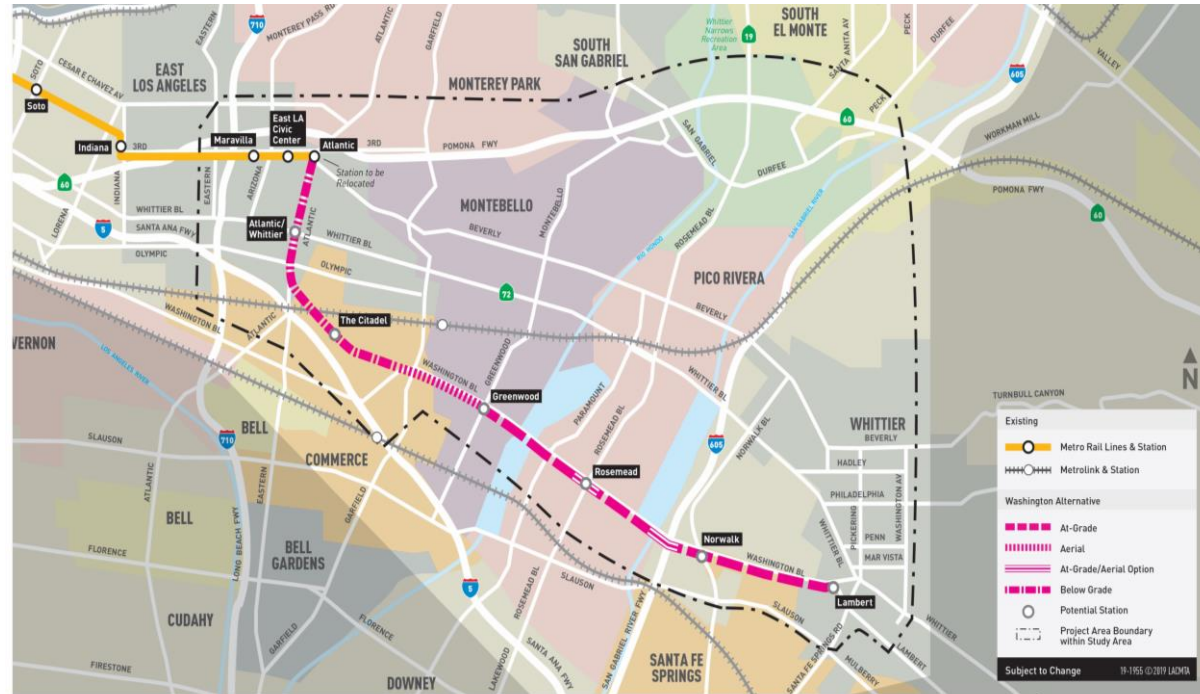

> Next Actions

- Finalize Community Based Organization strategy approach
- Refine the Draft Advanced Conceptual Engineering based on comments and evaluate cost saving opportunities along the alignment
- Proceed with a CEQA environmental analysis

Sepulveda Transit Corridor

> Status

- Environmental contract authorized at August 2020 Board Meeting
- Public outreach contract authorized at December 2020 Board Meeting
- Award of PDA contracts expected at March 2021 Board Meeting

> Key Activities

- Board and public review of proposed PDA proposals and contract awards.

> Next Actions

- Initiation of environmental scoping process. Environmental review process to be presented to the Board in April.
- Public scoping meetings in fall 2021.



NoHo to Pasadena BRT



> Status

- Draft EIR Public Review Period recently ended (October 26 – December 28, 2020)

> Key Activities

- Summary of public comments/responses underway (nearly 500 comments received)
- March 2021 – Conduct additional stakeholder/community outreach in response to comments received from Eagle Rock (“Beautiful Boulevard”) and City of Burbank

> Next Actions

- April 2021 – Staff response to December Board motion on optional left-side boarding vehicles
- May 2021 – Metro Board review of recommended Proposed Project

Metro's New Starts Grants Strategy Development Schedule

Board Staff Workshops

- December 14, 2020 – Workshop #1
- February 4, 2021 – Workshop #2
- March 3, 2021 – Workshop #3

Metro Board Action – April 2021

- New Starts priorities and strategies (CIG & EPD)
- FTA engagement and legislative strategy
